ROBERT ERVEN DITCH

No. 2245

GRAND RAPIDS TOWNSHIP

WOOD COUNTY

O.H. JONES ENG'R

1964

Ditch Book 139

The contractor shall replace all tile ends after completing the work so that no tile ends will extend from the bank more than one foot.
If the tile ends are broken during construction they shall be replaced with metal pipe of proper size and length for a permanent installation

Location of Tile

2+75 Rt. F.T.-4"	5+97 Rt. F.T.-4"	8+75 Rt. F.T.-4"
13+36 Rt. F.T.-4"	24+57 Lt. F.T.-6"	30+25-Rt.-F.T.-6"
33+14 Rt. F.T.-6"	33+45 Lt. V.T.-6"	33+70-Rt. F.T.-6"
34+10 Lt. V.T.-6"	34+64 Lt. V.T.-6"	35+22 Lt. V.T.-6"
35+22 Rt. V.T.-6"	36+05 Rt. V.T.-6"	36+33 Rt. V.T.-6"
36+90 Rt. V.T.-6"	37+50 Lt. V.T.-6"	38+09 Lt. V.T.-6"
38+50 Rt. V.T.-6"		

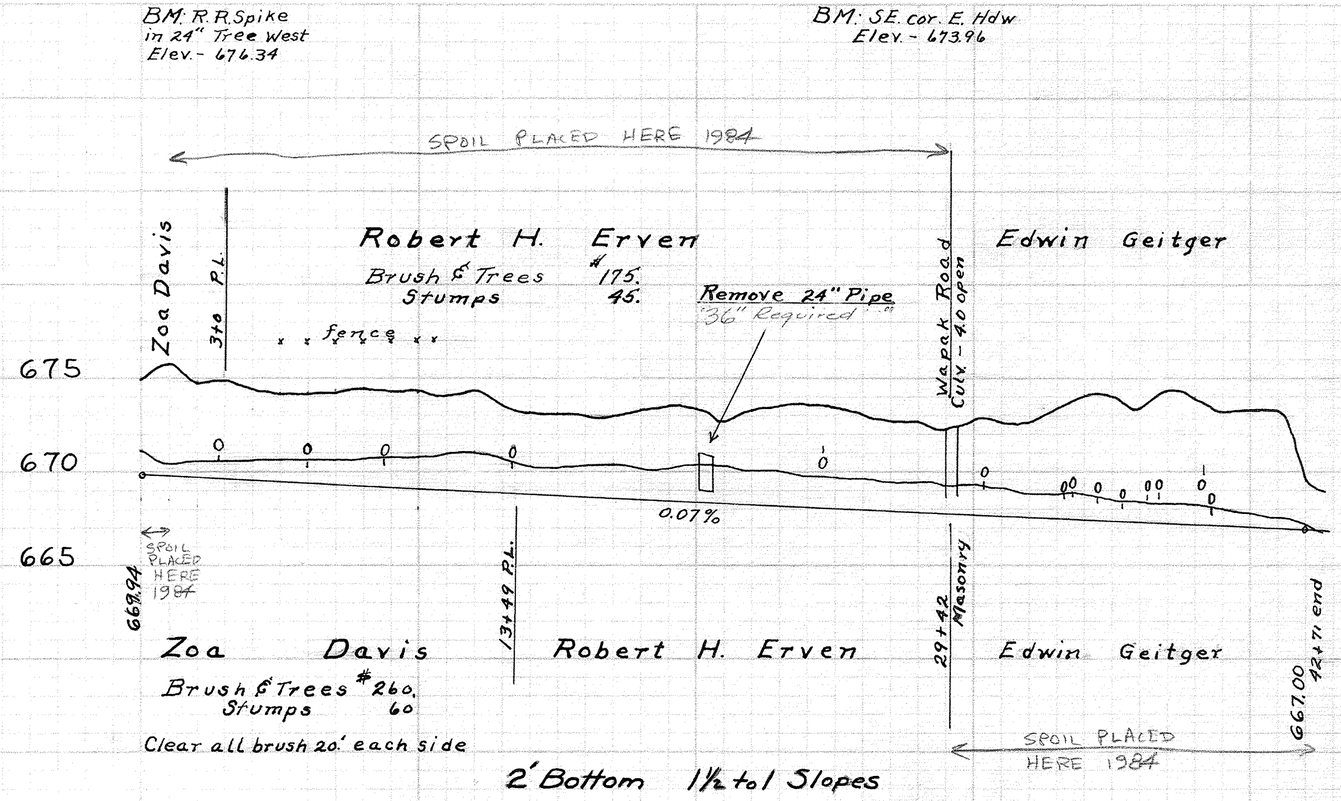

STATION	HUB ELEVATION	GRADE	CUT	CU. YDS.
0	675.96	669.94	5.02	
1	675.81	669.87	5.94	61
2	674.81	669.80	5.01	
3	674.86	669.73	5.13	44
4	674.42	669.66	4.76	
5	674.19	669.59	4.60	
6	674.24	669.52	4.74	44
7	674.37	669.45	4.92	
8	674.54	669.38	5.16	48
9	674.24	669.31	4.95	
10	674.22	669.24	4.98	53
11	674.00	669.17	4.83	
12	674.40	669.10	5.30	61
13	673.56	669.03	4.53	
14	673.22	668.96	4.26	49
15	673.11	668.89	4.22	
16	673.06	668.82	4.24	73
17	672.98	668.75	4.23	
18	673.34	668.68	4.66	77
19	673.53	668.61	4.92	
20	673.46	668.54	4.92	81
21	673.75	668.47	5.28	
22	673.34	668.40	4.94	110
23	673.53	668.33	5.20	
24	673.60	668.26	5.34	114
25	673.50	668.19	5.31	
26	673.00	668.12	4.88	89
27	672.72	668.05	4.67	
28	672.73	667.98	4.75	89
29	672.29	667.91	4.38	
30	672.84	667.84	5.00	89
31	672.74	667.77	4.97	
32	672.61	667.70	4.91	66
33	673.40	667.63	5.77	
34	674.07	667.56	6.51	61
35	674.05	667.49	6.56	
36	673.49	667.42	6.07	73
37	672.61	667.35	5.32	
38	672.33	667.28	5.05	69
39	671.61	667.21	4.40	
40	671.68	667.14	4.54	53
41	671.67	667.07	4.60	
42	669.84	667.00	2.54	40
				14

Total Total 1478
