EUGENE MILLER DITCH
№ 2259

Webester Twp. Wood Co. Ohio

B. F. Henning Co. Engineer

Ditch Book 136 Dec. 1945

Brush and spraying Lump $18.00

Brush will be sprayed same day cut, using 1 part esteron 245-DG in 24 parts oil

The present 36" pipe under route 582 will be replaced by the state highway department with a 54" Conc pipe to be furnished by the county - Station 103+40 to Sta. 107+15. Present Manholes to be replaced by new to accommodate 54" pipe

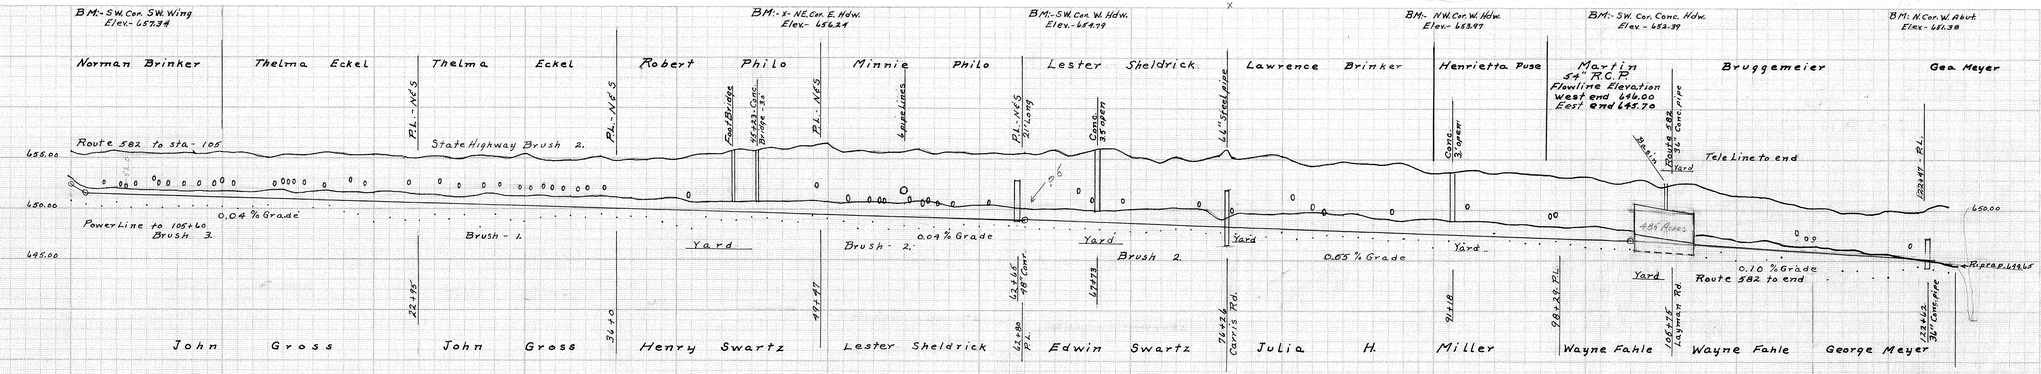

746 rod open ditch bottom cleanout

Station	Hub Elevation	Cut	Grade
0	655.60	6.25.50	9.08
1	655.30	6.24.80	8.82
2	655.03	6.24.44	8.17
3	654.76	6.24.40	8.14
4	654.52	6.24.34	8.24
5	654.32	6.24.32	8.20
6	654.38	6.24.28	8.16
7	654.24	6.24.24	8.17
8	654.49	6.24.20	8.21
9	654.60	6.24.16	8.28
10	654.60	6.24.12	8.48
11	654.59	6.24.08	8.49
12	654.63	6.24.04	8.49
13	654.69	6.24.00	8.49
14	654.76	6.23.96	8.49
15	654.85	6.23.92	8.49
16	654.98	6.23.88	8.50
17	655.08	6.23.84	8.54
18	655.21	6.23.80	8.57
19	655.34	6.23.76	8.59
20	655.47	6.23.72	8.62
21	655.53	6.23.68	8.64
22	655.58	6.23.64	8.64
23	655.64	6.23.60	8.64
24	655.68	6.23.56	8.62
25	655.74	6.23.52	8.61
26	655.79	6.23.48	8.59
27	655.79	6.23.44	8.57
28	655.77	6.23.40	8.57
29	655.73	6.23.36	8.57
30	655.74	6.23.32	8.58
31	655.82	6.23.28	8.54
32	655.76	6.23.24	8.52
33	655.79	6.23.20	8.51
34	655.74	6.23.16	8.48
35	655.73	6.23.12	8.52
36	655.72	6.23.08	8.54
37	655.74	6.23.04	8.54
38	655.81	6.23.00	8.51
39	655.88	6.22.96	8.54
40	655.95	6.22.92	8.54
41	655.94	6.22.88	8.57
42	655.91	6.22.84	8.57
43	655.89	6.22.80	8.59
44	655.88	6.22.76	8.59
45	655.87	6.22.72	8.61
46	655.86	6.22.68	8.61
47	655.87	6.22.64	8.63
48	655.87	6.22.60	8.63
49	655.87	6.22.56	8.63
50	655.87	6.22.52	8.64
51	655.91	6.22.48	8.63
52	655.93	6.22.44	8.59
53	655.94	6.22.40	8.54
54	655.98	6.22.36	8.54
55	656.03	6.22.32	8.54
56	656.07	6.22.28	8.54
57	656.09	6.22.24	8.54
58	656.10	6.22.20	8.54
59	656.12	6.22.16	8.54
60	656.13	6.22.12	8.54
61	656.13	6.22.08	8.54
62	656.13	6.22.04	8.54
63	656.12	6.22.00	8.54
64	656.11	6.21.96	8.54
65	656.09	6.21.92	8.54
66	656.07	6.21.88	8.54
67	656.04	6.21.84	8.54
68	656.00	6.21.80	8.54
69	655.97	6.21.76	8.54
70	655.93	6.21.72	8.54
71	655.90	6.21.68	8.54
72	655.90	6.21.64	8.57
73	655.91	6.21.60	8.57
74	655.88	6.21.56	8.59
75	655.88	6.21.52	8.59
76	655.91	6.21.48	8.59
77	655.95	6.21.44	8.59
78	655.97	6.21.40	8.57
79	655.98	6.21.36	8.56
80	655.97	6.21.32	8.56
81	655.95	6.21.28	8.56
82	655.93	6.21.24	8.56
83	655.91	6.21.20	8.56
84	655.88	6.21.16	8.56
85	655.87	6.21.12	8.56
86	655.89	6.21.08	8.56
87	655.90	6.21.04	8.56
88	655.91	6.21.00	8.56
89	655.95	6.20.96	8.56
90	655.97	6.20.92	8.56
91	655.98	6.20.88	8.56
92	655.99	6.20.84	8.56
93	655.99	6.20.80	8.56
94	655.98	6.20.76	8.56
95	655.97	6.20.72	8.56
96	655.96	6.20.68	8.56
97	655.95	6.20.64	8.56
98	655.93	6.20.60	8.56
99	655.92	6.20.56	8.56
100	655.89	6.20.52	8.56
101	655.87	6.20.48	8.56
102	655.85	6.20.44	8.56
103	655.82	6.20.40	8.56
104	655.79	6.20.36	8.56
105	655.76	6.20.32	8.56
106	655.73	6.20.28	8.56
107	655.70	6.20.24	8.56
108	655.68	6.20.20	8.56
109	655.66	6.20.16	8.56
110	655.65	6.20.12	8.56
111	655.64	6.20.08	8.56
112	655.63	6.20.04	8.56
113	655.62	6.20.00	8.56
114	655.61	6.19.96	8.56
115	655.60	6.19.92	8.56
116	655.60	6.19.88	8.55
117	655.63	6.19.84	8.55
118	655.62	6.19.80	8.55
119	655.62	6.19.76	8.55
120	655.77	6.19.72	8.57
121	655.81	6.19.68	8.57
122	655.84	6.19.64	8.57
123	655.83	6.19.60	8.57
124	655.82	6.19.56	8.57
125	655.81	6.19.52	8.57
126	655.80	6.19.48	8.57
127	655.79	6.19.44	8.57
128	655.78	6.19.40	8.57

DEC 27 1968
