MINNIE M. DAUER
DITCH № 2265
Washing Twp. Wood Co. Ohio
B. F. Henning Engineer Book 138

All stumps, and all brush less than two feet high shall be treated with brush and stump killer and killed.-Contractor will be compeled to complete this item.

Two foot bottom and sloped as shown on cross-sections

All brush and stumps must be removed from spoil

Drive culvert at 12+36 shall be removed. If replaced it shall be at proper grade

Culvert a Cross Creek Road to be lowered by county.

0	667.75	663.30	4.45	
1	667.79	663.25	4.54	
2	666.93	663.20	3.73	119
3	666.63	663.15	3.48	
4	666.69	663.10	3.59	81
5	666.92	663.05	3.87	
6	667.12	663.00	4.12	65
7	667.02	662.95	4.07	
8	667.05	662.90	4.15	81
9	666.45	662.85	3.60	
10	667.53	662.80	4.73	100
11	667.25	662.75	4.50	
12	667.71	662.70	5.01	104
13	668.17	662.65	5.52	
14	668.81	662.60	6.21	104
15	669.78	662.55	7.18	
16	669.28	662.50	6.78	126
17	668.72	662.45	6.27	
18	668.10	662.40	5.70	89
19	668.46	662.35	6.11	
20	668.24	662.30	5.94	40
21	668.27	662.25	6.02	
22	668.48	662.20	6.28	40
23	667.95	662.15	5.80	
24	667.74	662.10	5.64	40
25	667.87	662.05	5.82	
26	667.54	662.00	5.54	40
27	667.48	661.95	5.53	
28	667.78	661.90	5.88	40
29	667.98	661.85	6.13	
30	668.44	661.80	6.64	40
31	668.05	661.75	6.30	
32	667.97	661.70	6.27	40
33	667.83	661.65	6.18	
34	668.08	661.60	6.48	40
35	668.11	661.55	6.56	
36	668.83	661.50	7.33	40
36+60		660.58		
37	667.74	660.47	7.27	
38	666.98	660.25	6.73	70
39	666.84	660.03	6.81	
40	666.96	659.81	7.15	119
40+50		659.70		
41	666.05	659.20	6.85	
2	666.12	659.06	6.06	137
3	665.90	658.92	6.98	
4	665.77	658.78	6.99	200
5	665.97	658.64	7.33	
6	665.66	658.50	7.16	251
7	665.50	658.36	7.14	
8	665.42	658.22	7.20	277
9	664.67	658.08	6.59	
50	665.32	657.94	7.38	244
51	665.12	657.80	7.32	
52	665.31	657.66	7.65	226
53	665.23	657.52	7.71	
54	664.91	657.38	7.53	263
55	664.08	657.24	6.84	
56	664.54	657.10	7.44	193
57	664.18	656.96	7.22	
58	663.33	656.82	6.51	89
59	662.71	656.68	6.03	
60	662.55	656.54	6.01	40
61	662.66	656.40	6.26	
62	661.96	656.26	5.70	40
63	662.38	656.12	6.26	
64	661.77	655.98	5.79	40
65	662.10	655.84	6.26	
66	661.60	655.70	5.90	40
67	661.47	655.56	5.91	
68	661.21	655.42	5.79	40
69	660.81	655.28	4.53	
70	662.71	655.14	7.57	40
71	661.99	655.00	4.99	
72	663.03	654.86	8.17	40
73	662.91	654.72	8.19	
74	659.83	654.58	5.25	48
75	660.21	654.44	5.77	
76	658.77	654.30	4.47	40
76+16				8
Total Cu. Yds				3666

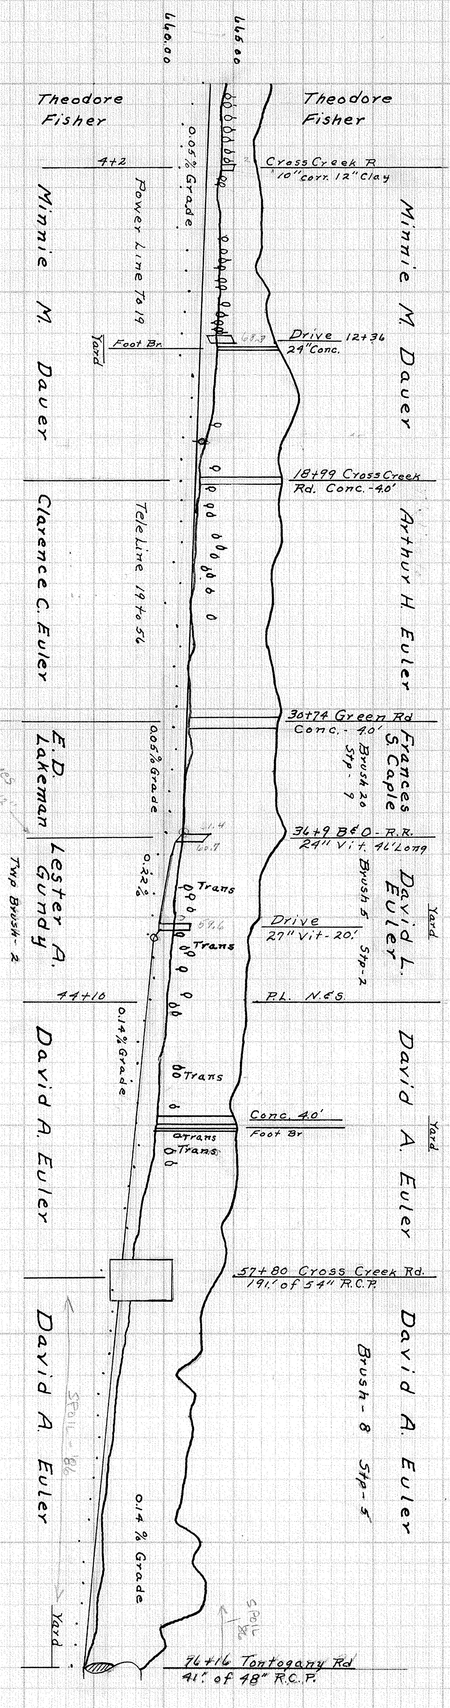

M.F. SEP 10 1968
